


Integrated Programme of Works

Joint Venture of RM Enterprise Limited and Inkript Securities S.A.L | RFP No. MW-PPPC-546386-GO-RFB, Provision of a Turnkey Solution for the Rehabilitation, Upgrading and Commissioning of the Central Printing Facility

Weeks are counted from the Effective Date: week 1 is the first week after it. Phases 1 to 10 are the lines of the Implementation Schedule, and black diamonds are its contractual milestones. Each task is assigned to the party that performs it: RME is RM Enterprise Limited and Inkript is Inkript Securities S.A.L, the members of the joint venture.

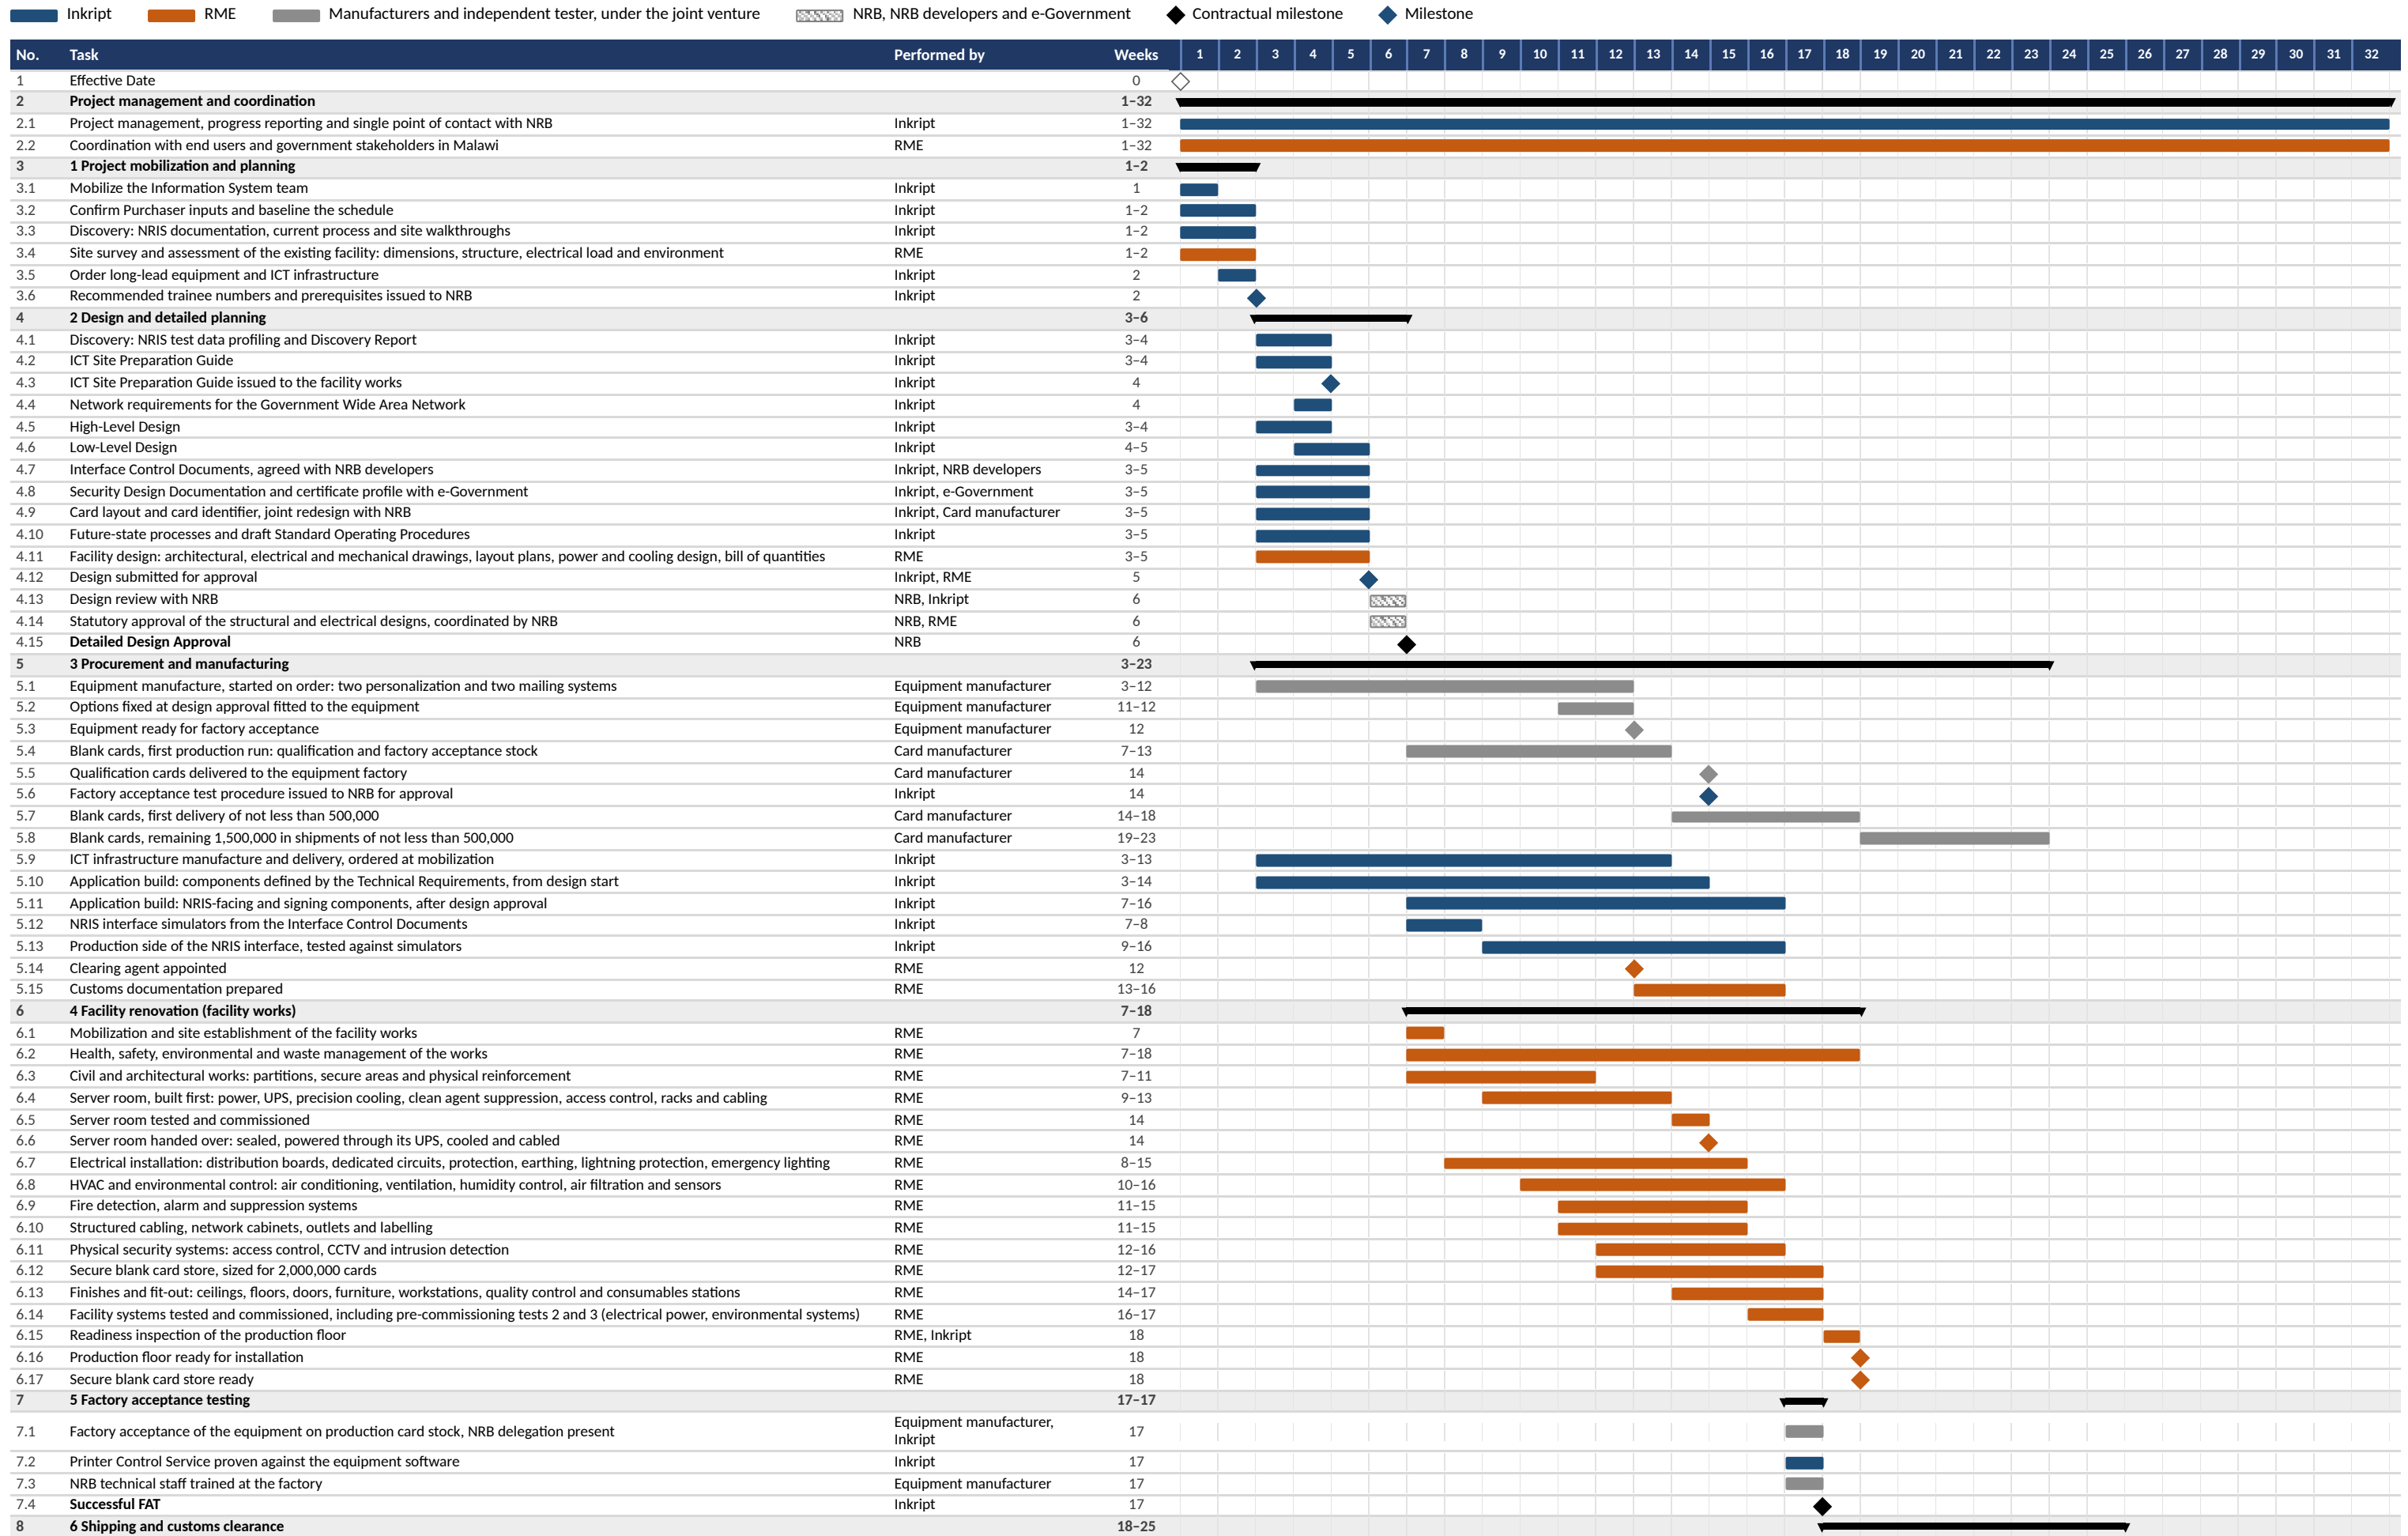

No.	Task	Performed by	Weeks	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	32
8.1	Shipping of the personalization and mailing equipment	Inkript	18–19																																
8.2	Customs clearance and delivery to NRB	RME	20																																
8.3	Equipment delivered on site	RME	20																																
8.4	First card delivery shipped, cleared and delivered to NRB	Inkript, RME	19–20																																
8.5	First card delivery on site	RME	20																																
8.6	Remaining card shipments cleared and delivered to NRB	Inkript, RME	24–25																																
8.7	All 2,000,000 cards on site, before commissioning	RME	25																																
9	7 Installation and site acceptance testing		15–26																																
9.1	ICT infrastructure delivered to site, inspected and racked	RME, Inkript	15																																
9.2	NRB technical staff shadow installation and commissioning	NRB	15–26																																
9.3	Platform build: application and database clusters, storage array, directory, database, security, non-production environments	Inkript	16																																
9.4	Hardware security module installed at the primary site, key ceremony, certificate signing request to e-Government	Inkript	16																																
9.5	Secondary environment deployed at Blantyre, its hardware security module enrolled, and replication established	Inkript	16–18																																
9.6	Application deployed and integrated with the directory	Inkript	17																																
9.7	Pre-Commissioning Test Program submitted to NRB for approval	Inkript	17																																
9.8	Early integration with NRIS: interfaces tested as NRB delivers them	Inkript, NRB developers	18–22																																
9.9	Integration with NRIS completed against NRB's delivered side	Inkript, NRB developers	23–24																																
9.10	Pre-commissioning tests of the ICT estate, Table A 4, 5, 8 and 13	Inkript	19–20																																
9.11	Performance testing of the software, and security testing	Inkript	20–21																																
9.12	Equipment inspected on delivery, unpacked and placed	Inkript, RME	21																																
9.13	Equipment installed and commissioned by the manufacturer's engineers	Equipment manufacturer	21–23																																
9.14	Critical Spare Parts List submitted to NRB for approval	Inkript	24																																
9.15	User acceptance testing with NRIS stakeholders	Inkript, NRB	24–25																																
9.16	Security Operations Center integrated with NRB's Security Operations Center	Inkript	25																																
9.17	Independent penetration testing of the full deployed configuration	Independent penetration tester	24																																
9.18	Pre-commissioning tests of the equipment and integration, Table A 1, 6, 7, 9 to 12, 14 and 16	Inkript	24–26																																
9.19	Pilot production of 500 to 1,000 test cards, not issued to citizens	Inkript	26																																
9.20	Installation and SAT complete	Inkript	26																																
10	8 Training and knowledge transfer		24–28																																
10.1	User training, groups one and two, one for each shift	Inkript	25–26																																
10.2	Technical training, NRB technical trainers co-delivering	Inkript	26–27																																
10.3	Management training	Inkript	26																																
10.4	User training, cover group, delivered by NRB trainers under observation	NRB	27–28																																
10.5	Training venues, logistics and trainee coordination	RME	24–28																																
10.6	Facility training: facility operations, electrical, HVAC, fire and security systems, preventive maintenance, emergency procedures	RME	27–28																																
10.7	Training completed	Inkript	28																																
11	9 System commissioning and performance testing		27–30																																
11.1	Operational acceptance tests 1 to 12, 14 and 15	NRB, Inkript	27																																
11.2	Sustained production stability and multi-shift operation, tests 2 and 13	NRB, Inkript	27–28																																
11.3	Operational independence, test 16	NRB	28																																
11.4	Final acceptance demonstration, test 17, ten working day observation	NRB, Inkript	29–30																																
11.5	System commissioned	Inkript	30																																
11.6	Warranty and support documentation delivered	Inkript	30																																
12	10 Handover, go-live and closure		31–32																																
12.1	As-built documentation, prepared progressively from week 27, finalized	Inkript	31–32																																
12.2	Transfer of Security Operations Center operation to NRB	Inkript	31–32																																
12.3	Stabilization: resident engineers on every shift, daily review with NRB	Inkript	31–32																																
12.4	Facility as-built drawings, test reports, manuals, warranties and maintenance schedules delivered	RME	31–32																																
12.5	Full handover and go-live	Inkript, RME	32																																
13	Dependencies on the Purchaser and other parties		2–25																																
13.1	NRIS documentation received (NRB)	NRB	1																																
13.2	Access to the NRIS test environment for profiling (NRB)	NRB	2																																
13.3	Card design decisions (NRB)	NRB	5																																
13.4	QR code specification (NRB)	NRB	5																																
13.5	Certificate profile and signing request procedure (e-Government)	e-Government	5																																
13.6	Observation period for the final acceptance demonstration agreed (NRB)	NRB	5																																
13.7	Factory acceptance delegation nominated (NRB)	NRB	11																																
13.8	Dedicated electrical connection to the facility live (NRB)	NRB	12																																
13.9	Technical trainees nominated (NRB)	NRB	14																																
13.10	Government Wide Area Network provisioned (NRB, e-Government)	NRB, e-Government	15																																
13.11	Access, floor space, power and cooling at the Blantyre data center (NRB)	NRB	15																																
13.12	Purchaser documents for customs clearance (NRB)	NRB	16																																
13.13	Connectivity from the facility to the NRIS test environment (NRB)	NRB	17																																
13.14	User trainees nominated (NRB)	NRB	19																																
13.15	NRIS side of the interface (NRB developers)	NRB developers	7–22																																
13.16	NRIS side of the interface ready for integration (NRB)	NRB developers	22																																
13.17	Document Signer certificate issue (e-Government)	e-Government	17–19																																
13.18	Document Signer certificate issued (e-Government)	e-Government	19																																
13.19	NRB Security Operations Center integration details (NRB)	NRB	24																																
13.20	Remote support access arranged (NRB, e-Government)	NRB, e-Government	25																																
